

Project Time Management



Importance of Project Schedules

- ❑ Managers often cite delivering projects on time as one of their biggest challenges
- ❑ Time has the least amount of flexibility; it passes no matter what happens on a project
- ❑ Schedule issues are the main reason for conflicts on projects, especially during the second half of projects

Project Time Management Processes

- **Planning schedule management:** determining the policies, procedures, and documentation that will be used for planning, executing, and controlling the project schedule
- **Defining activities:** identifying the specific activities that the project team members and stakeholders must perform to produce the project deliverables
- **Sequencing activities:** identifying and documenting the relationships between project activities
- **Estimating activity resources:** estimating how many **resources** a project team should use to perform project activities
- **Estimating activity durations:** estimating the number of work periods that are needed to complete individual activities
- **Developing the schedule:** analyzing activity sequences, activity resource estimates, and activity duration estimates to create the project schedule
- **Controlling the schedule:** controlling and managing changes to the project schedule

Project Time Management Summary

Planning

Process: **Plan schedule management**

Outputs: Schedule management plan

Process: **Define activities**

Outputs: Activity list, activity attributes, milestone list, project management plan updates

Process: **Sequence activities**

Outputs: Project schedule network diagrams, project documents updates

Process: **Estimate activity resources**

Outputs: Activity resource requirements, resource breakdown structure, project documents updates

Process: **Estimate activity durations**

Outputs: Activity duration estimates, project documents updates

Process: **Develop schedule**

Outputs: Schedule baseline, project schedule, schedule data, project calendars, project management plan updates, project documents updates

Monitoring and Controlling

Process: **Control schedule**

Outputs: Work performance information, schedule forecasts, change requests, project management plan updates, project documents updates, organizational process assets updates

Project Start

Project Finish

Planning Schedule Management

- The project team uses expert judgment, analytical techniques, and meetings to develop the schedule management plan
- A schedule management plan includes:
 - The scheduling methodology
 - Level of accuracy and units of measure
 - Rules of performance measurement
 - Reporting formats
 - Process descriptions

Defining Activities

- An **activity** or **task** is an element of work normally found on the work breakdown structure (WBS) that has an expected duration, a cost, and resource requirements
- Activity definition involves developing a more detailed WBS and supporting explanations to understand all the work to be done so you can develop realistic cost and duration estimates

Activity Lists and Attributes

- An **activity list** is a tabulation of activities to be included on a project schedule that includes
 - the activity name
 - an activity identifier or number
 - a brief description of the activity
- **Activity attributes** provide more information such as predecessors, successors, logical relationships, leads and lags, resource requirements, constraints, imposed dates, and assumptions related to the activity

Sequencing Activities

- Involves reviewing activities and determining dependencies
- A **dependency** or **relationship** is the sequencing of project activities or tasks
- You *must* determine dependencies to use the *critical path analysis*


Three types of Dependencies

- ❑ **Mandatory dependencies:** The relationships between project activities that are **inherent** or **unavoidable**. Also called **hard logic** or **hard dependencies**.
- ❑ **Discretionary dependencies:** Defined by the project team, sometimes referred to as soft logic. The project manager or team **decides** to use it for better workflow, efficiency, or experience — but they **can be changed** if needed
- ❑ **External dependencies:** involve relationships between project and non-project activities. E.g. receive government approval for any project

Network Diagrams

- Network diagrams are the preferred technique for showing activity sequencing
- A **network diagram** is a schematic display of the logical relationships among, or sequencing of, project activities
- Two main formats are:
 - The arrow diagramming method, and
 - Precedence diagramming methods

Network Diagram for Project X

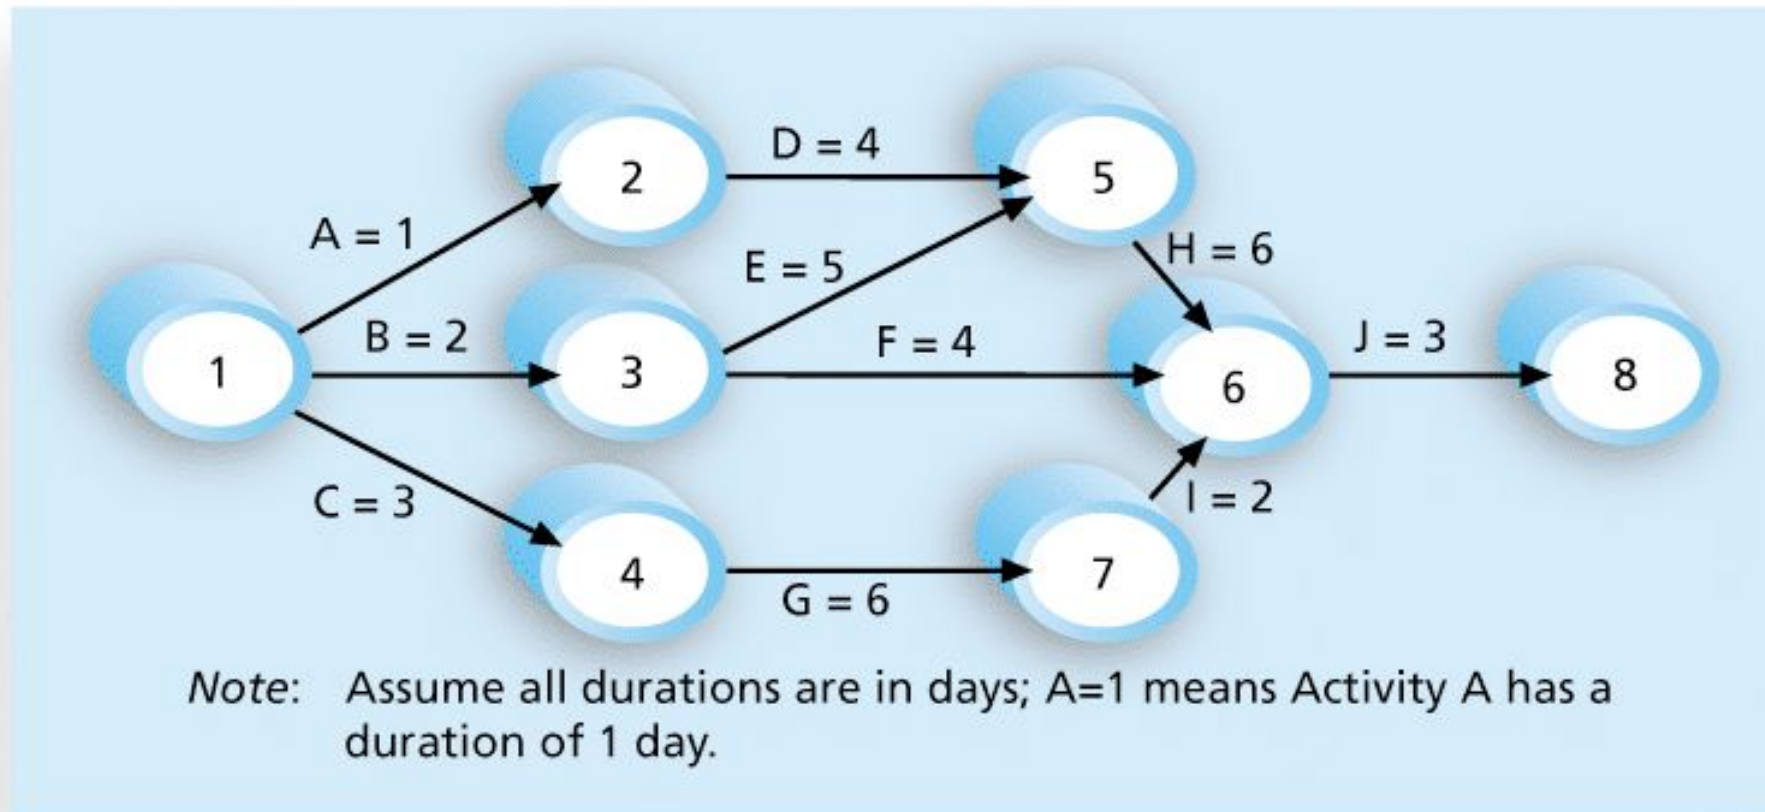

Arrow Diagramming Method (ADM)

- Also called activity-on-arrow (AOA) network diagrams
- Activities are represented by arrows
- Nodes or circles are the starting and ending points of activities
- Can only show finish-to-start dependencies

Process for Creating AOA Diagrams

1. Find all of the activities that start at node 1. Draw their finish nodes and draw arrows between node 1 and those finish nodes. Put the activity letter or name and duration estimate on the associated arrow
2. Continuing to draw the network diagram, working from left to right. Look for bursts and merges. **Bursts** occur when a single node is followed by two or more activities. A **merge** occurs when two or more nodes precede a single node
3. Continue drawing the project network diagram until all activities are included on the diagram that have dependencies
4. As a rule of thumb, all arrowheads should face toward the right, and no arrows should cross on an AOA network diagram




Precedence Diagramming Method (PDM)

- Activities are represented by boxes
- Arrows show relationships between activities
- More popular than ADM method and used by project management software
- Better at showing different types of dependencies


Task Dependency Types

Task dependencies

The nature of the relationship between two linked tasks. You link tasks by defining a dependency between their finish and start dates. For example, the "Contact caterers" task must finish before the start of the "Determine menus" task. There are four kinds of task dependencies in Microsoft Project.

Task dependency	Example	Description
Finish-to-start (FS)		Task (B) cannot start until task (A) finishes.
Start-to-start (SS)		Task (B) cannot start until task (A) starts.
Finish-to-finish (FF)		Task (B) cannot finish until task (A) finishes.
Start-to-finish (SF)		Task (B) cannot finish until task (A) starts.

Sample PDM Network Diagram

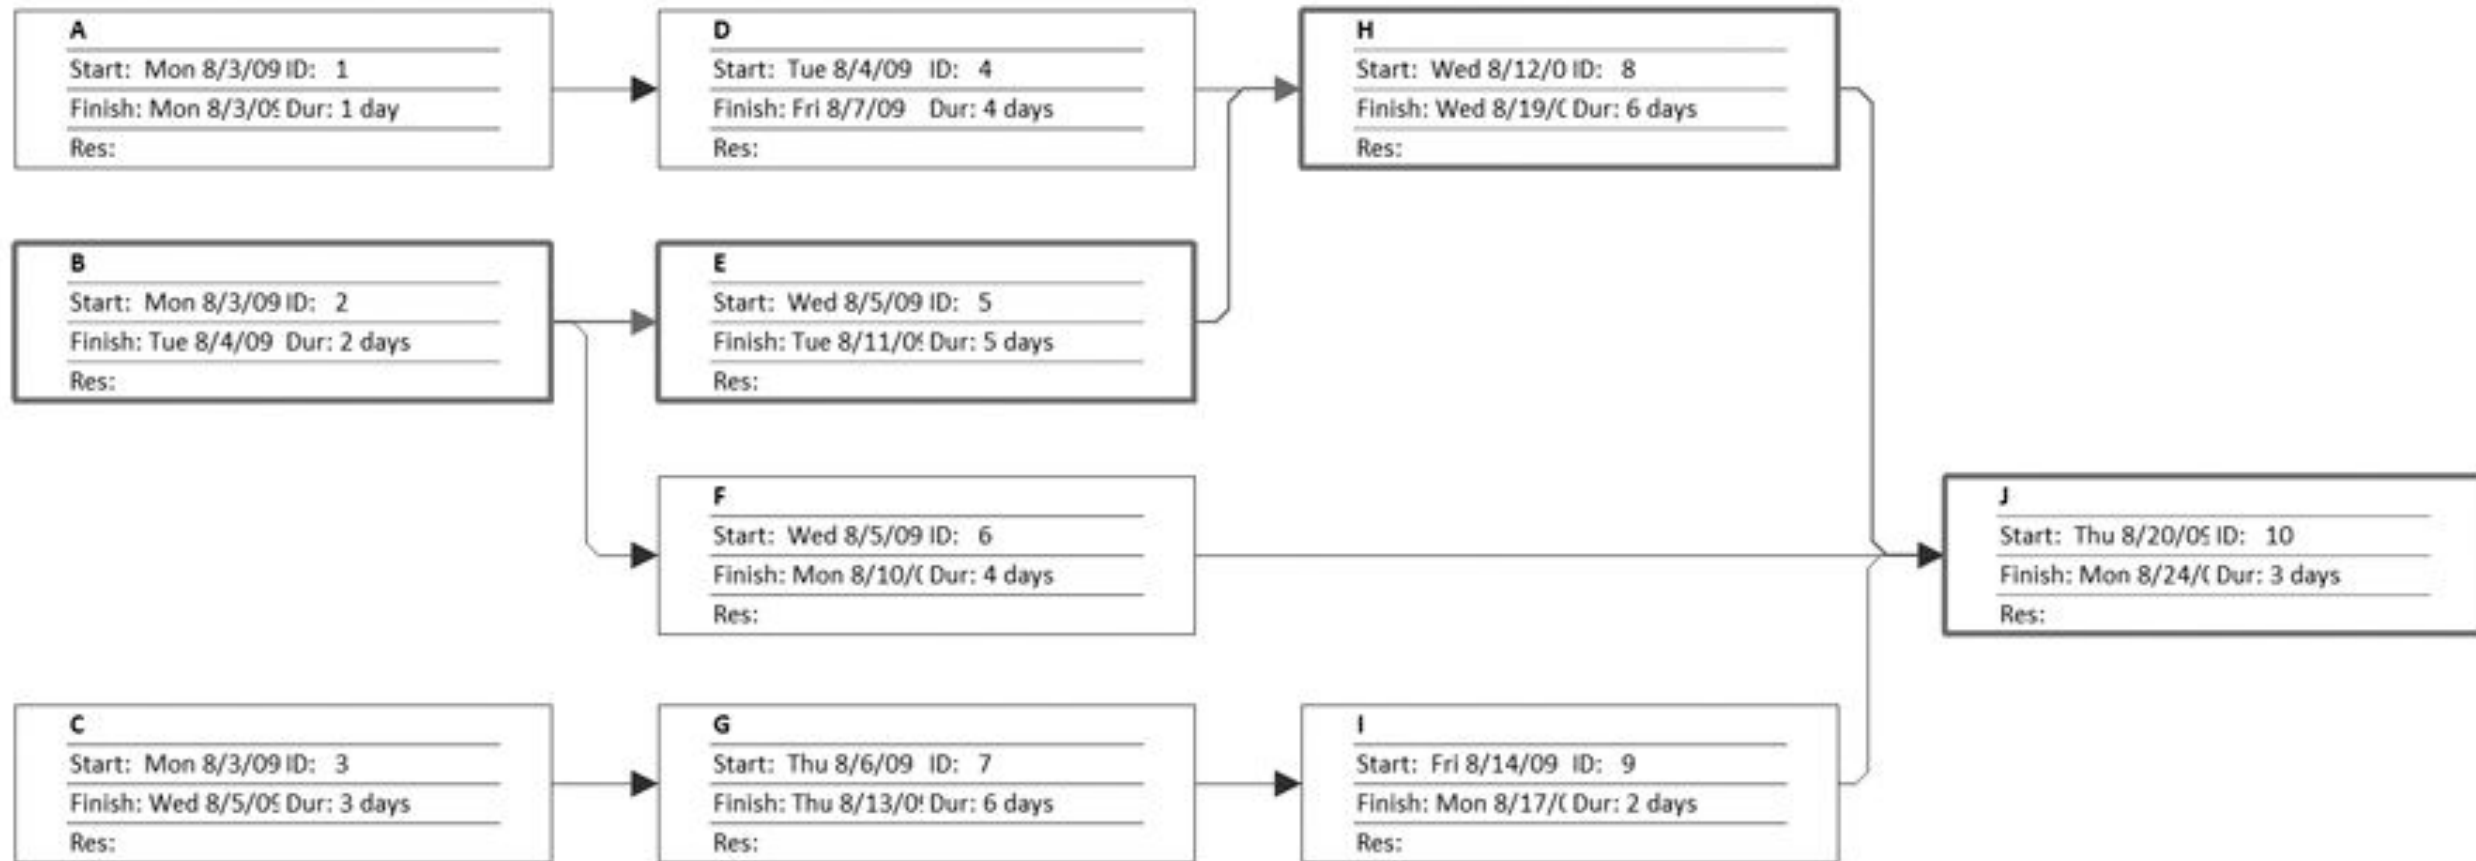

Estimating Activity Resources

- ▣ **Resources** are people, equipment, and materials
- ▣ Before estimating activity durations, you must have a good idea of the quantity and type of resources that will be assigned to each activity.
- ▣ Consider important issues in estimating resources
 - How difficult will it be to do specific activities on this project?
 - What is the organization's history in doing similar activities?
 - Are the required resources available?

Activity Duration Estimating

- **Duration** is the **total time** that an activity takes to complete — from **start to finish** — including working time and waiting time (like weekends or breaks).
 - A task starts on Monday and finishes on Friday → **Duration = 5 days**
- **Effort** is the **total amount of work or labor time** (in work hours or workdays) that people actually spend working on an activity.
 - If two people each work 4 hours per day for 5 days →
Effort = $2 \times 4 \times 5 = 40$ person-hours

Three-Point Estimates

- Instead of providing activity estimates as a discrete number, such as four weeks, it's often helpful to create a **three-point estimate**
 - an estimate that includes an **optimistic, most likely, and pessimistic estimate**, such as three weeks for the optimistic, four weeks for the most likely, and five weeks for the pessimistic estimate
- Three-point estimates are needed for PERT and Monte Carlo simulations


Developing the Schedule

- The ultimate goal is to create a realistic project schedule that provides a basis for monitoring project progress for the time dimension of the project
- Important tools and techniques include Gantt charts, critical path analysis, and critical chain scheduling, and PERT analysis

Gantt Charts


- **Gantt charts** provide a standard format for displaying project schedule information by listing project activities and their corresponding start and finish dates in a calendar format
- Symbols include:
 - A black diamond: a milestones
 - Thick black bars: summary tasks
 - Lighter horizontal bars: durations of tasks
 - Arrows: dependencies between tasks

Gantt Chart for Project X

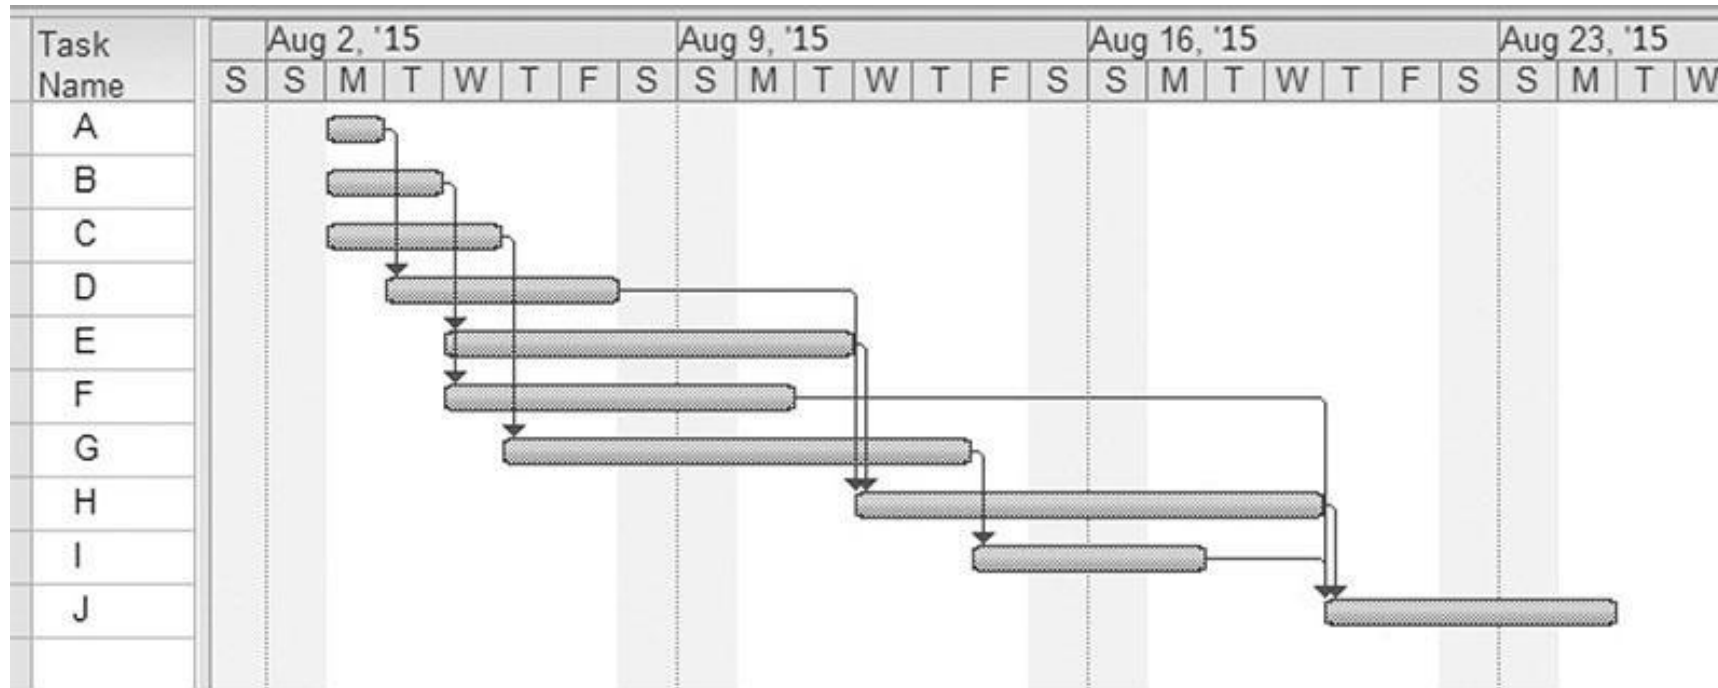

Used with permission from Microsoft Corporation

Gantt Chart for Software Launch Project

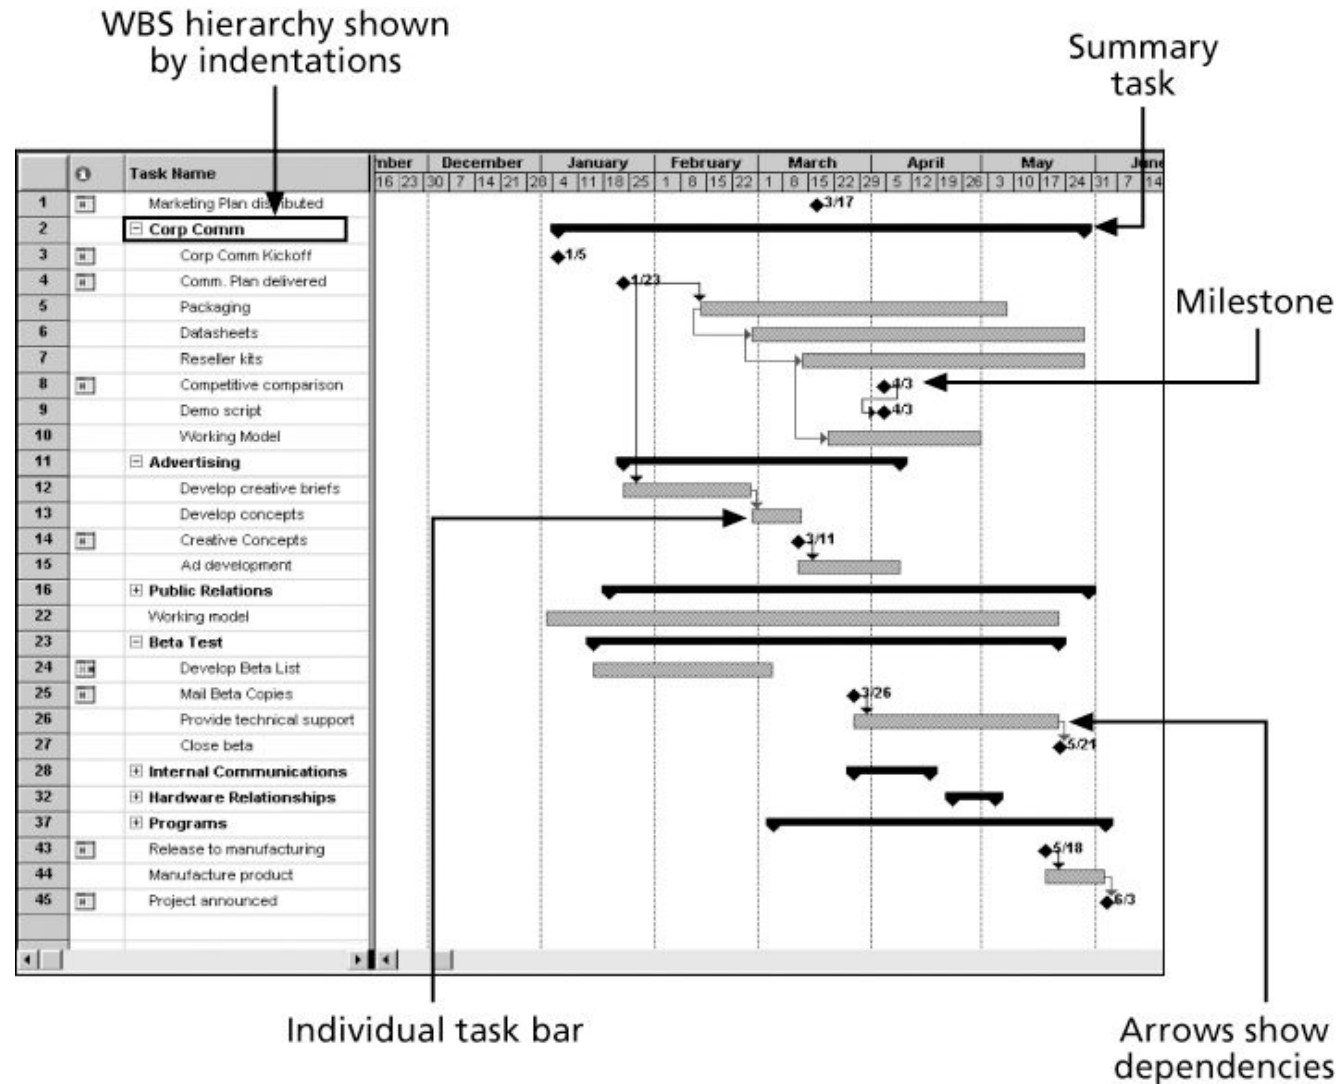

Adding Milestones to Gantt Charts

- Many people like to focus on meeting milestones, especially for large projects
- Milestones emphasize important events or accomplishments on projects
- Normally create milestone by entering tasks with a zero duration, or you can mark any task as a milestone

SMART Criteria

- Milestones should be
 - **S**pecific
 - **M**easurable
 - **A**ssignable
 - **R**ealistic
 - **T**ime-framed


Critical Path Method (CPM)

- The Critical Path Method is the sequence of scheduled activities that determines the project's duration.
- A **critical path** for a project is the series of activities that determines the *earliest time* by which the project can be completed
- The critical path is the *longest path* through the network diagram and has the least amount of slack or float
- **Slack** or **float** is the amount of time an activity may be delayed without delaying a succeeding activity or the project's finish date

Calculating the Critical Path

- First, develop a good network diagram
- Add the duration estimates for all activities on each path through the network diagram
- The longest path is the critical path
- If one or more of the activities on the critical path takes longer than planned, the whole project schedule will slip *unless* the project manager takes corrective action

Determining the Critical Path for Project X

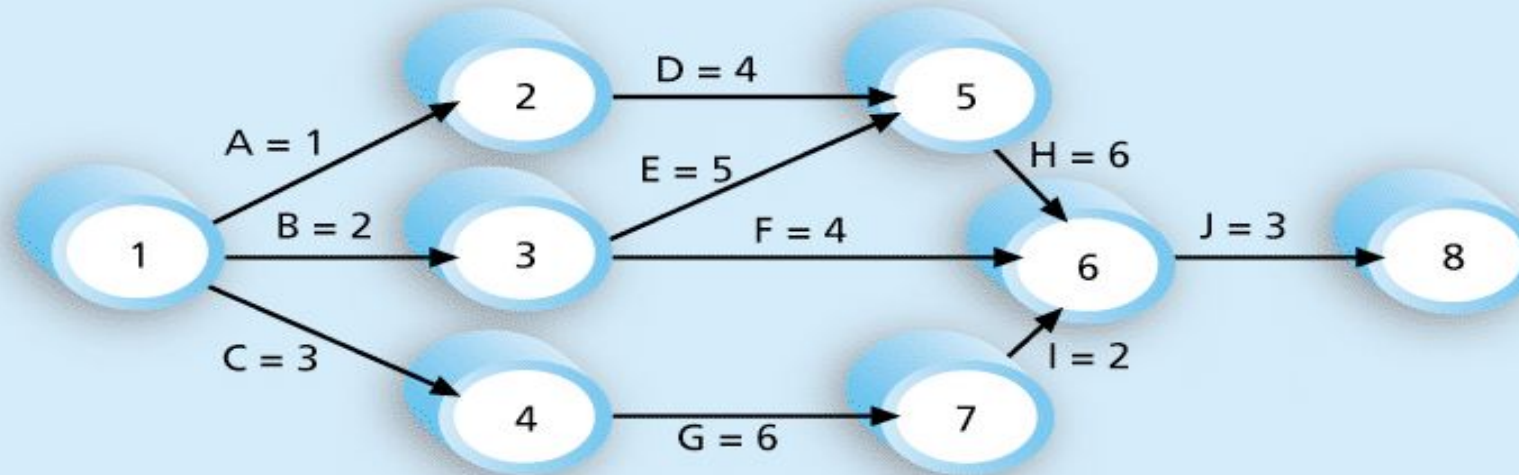

Note: Assume all durations are in days.

Path 1: A-D-H-J Length = $1+4+6+3 = 14$ days

Path 2: B-E-H-J Length = $2+5+6+3 = 16$ days

Path 3: B-F-J Length = $2+4+3 = 9$ days

Path 4: C-G-I-J Length = $3+6+2+3 = 14$ days

Since the critical path is the longest path through the network diagram, Path 2, B-E-H-J, is the critical path for Project X.

Using Critical Path Analysis to Make Schedule Trade-offs

- ▣ **Free slack** or **free float** is the amount of time an activity can be delayed without delaying the early start of any immediately following activities
- ▣ **Total slack** or **total float** is the amount of time an activity may be delayed from its early start without delaying the planned project finish date
- ▣ A **forward pass** through the network diagram determines the early start and finish dates
- ▣ A **backward pass** determines the late start and finish dates

Example of Calculating the Critical Path

- List Project Tasks and Estimate their Duration

Task Name	Estimated Duration
A	12
B	4
C	15
D	12
E	10
F	7

Example of Calculating the Critical Path

□ Identify Task Dependencies


Task Name	Preceding Tasks	Estimated Duration
A		12
B		4
C	A	15
D	B	12
E	C	10
F	D	7

Example of Calculating the Critical Path

- Create a Critical Path Diagram
 - Every project task has a start and finish time.
 - **Earliest start time (ES)**
 - **Earliest finish time (EF)**
 - **Latest start time (LS)**
 - **Latest finish time (LF)**
 - **Slack or float**

Example of Calculating the Critical Path


Task Name	Preceding Tasks	Estimated Duration
A		12
B		4
C	A	15
D	B	12
E	C	10
F	D	7

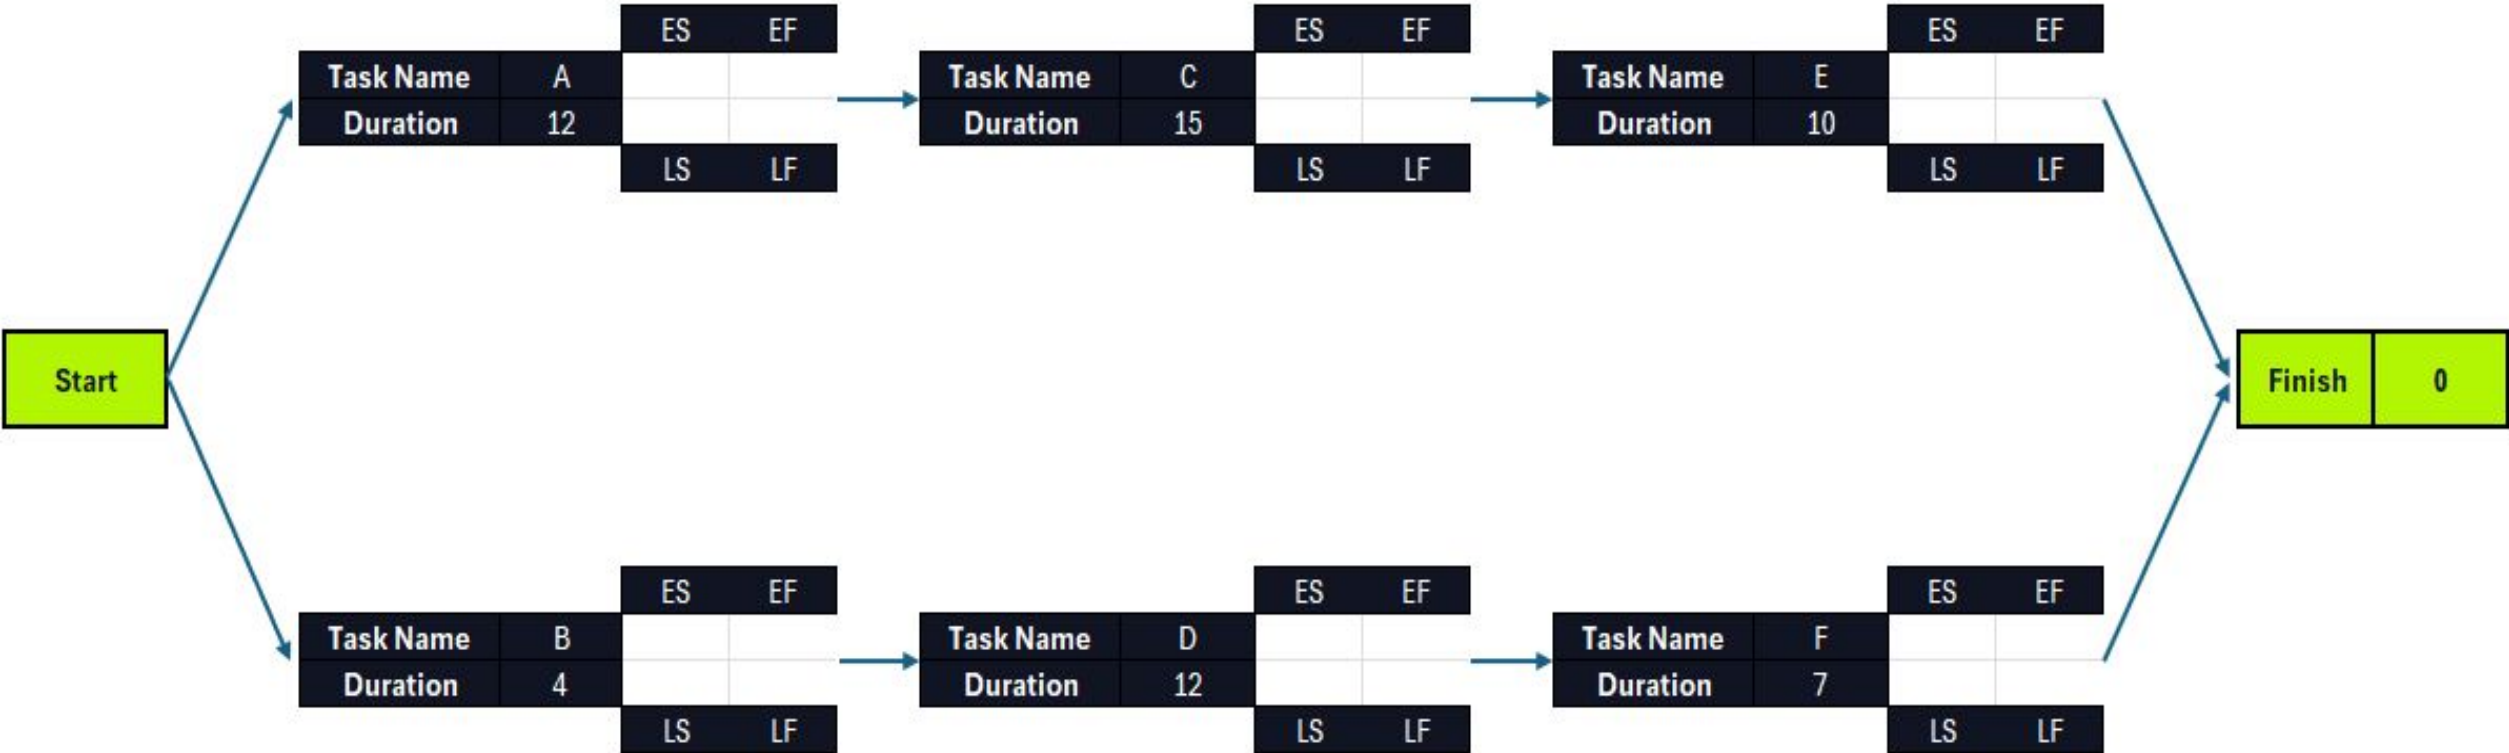

Example of Calculating the Critical Path

- Use the Critical Path Algorithm Formulas
 - Calculate the ES and EF and slack using the critical path **Forward Pass** formula.

Task Name	Preceding Tasks	Estimated Duration
A		12
B		4
C	A	15
D	B	12
E	C	10
F	D	7

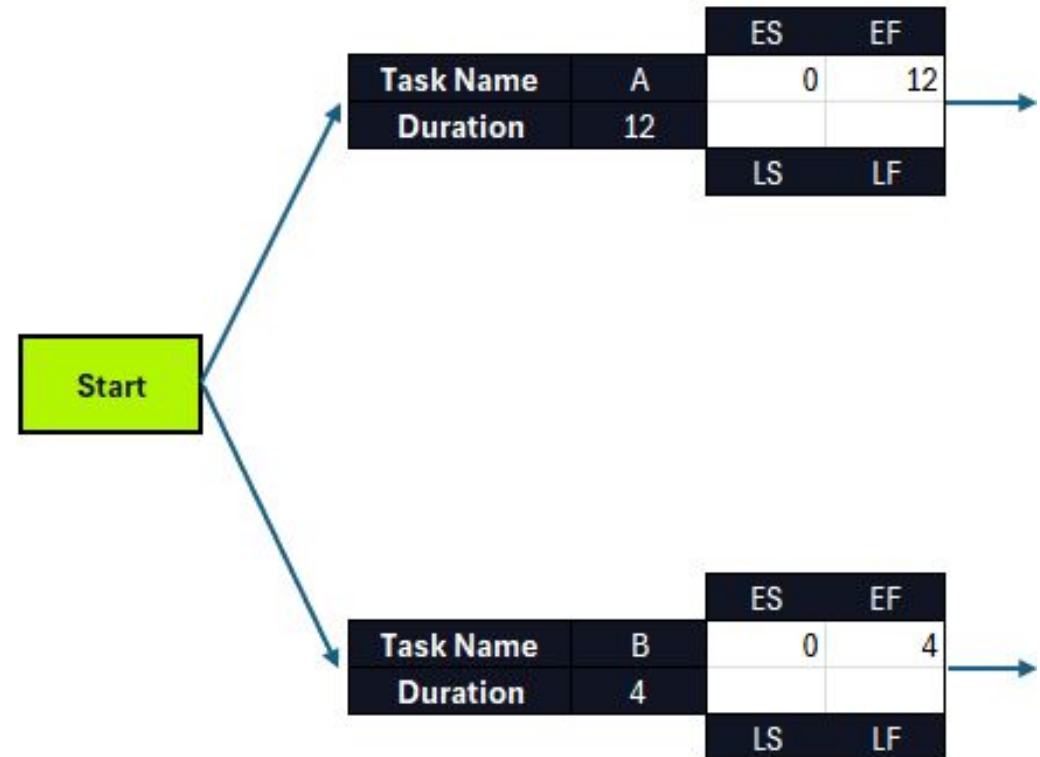

Example of Calculating the Critical Path

Task Name	Preceding Tasks	Estimated Duration
A		12
B		4
C	A	15
D	B	12
E	C	10
F	D	7

		ES	EF
Task Name	C	12	27
Duration	15		
		LS	LF

		ES	EF
Task Name	E	27	37
Duration	10		
		LS	LF

		ES	EF
Task Name	D	4	16
Duration	12		
		LS	LF

		ES	EF
Task Name	F	16	23
Duration	7		
		LS	LF


Finish

Example of Calculating the Critical Path

- Calculate the LS and LF and slack using the critical path **Backward Pass** formula.



Example of Calculating the Critical Path

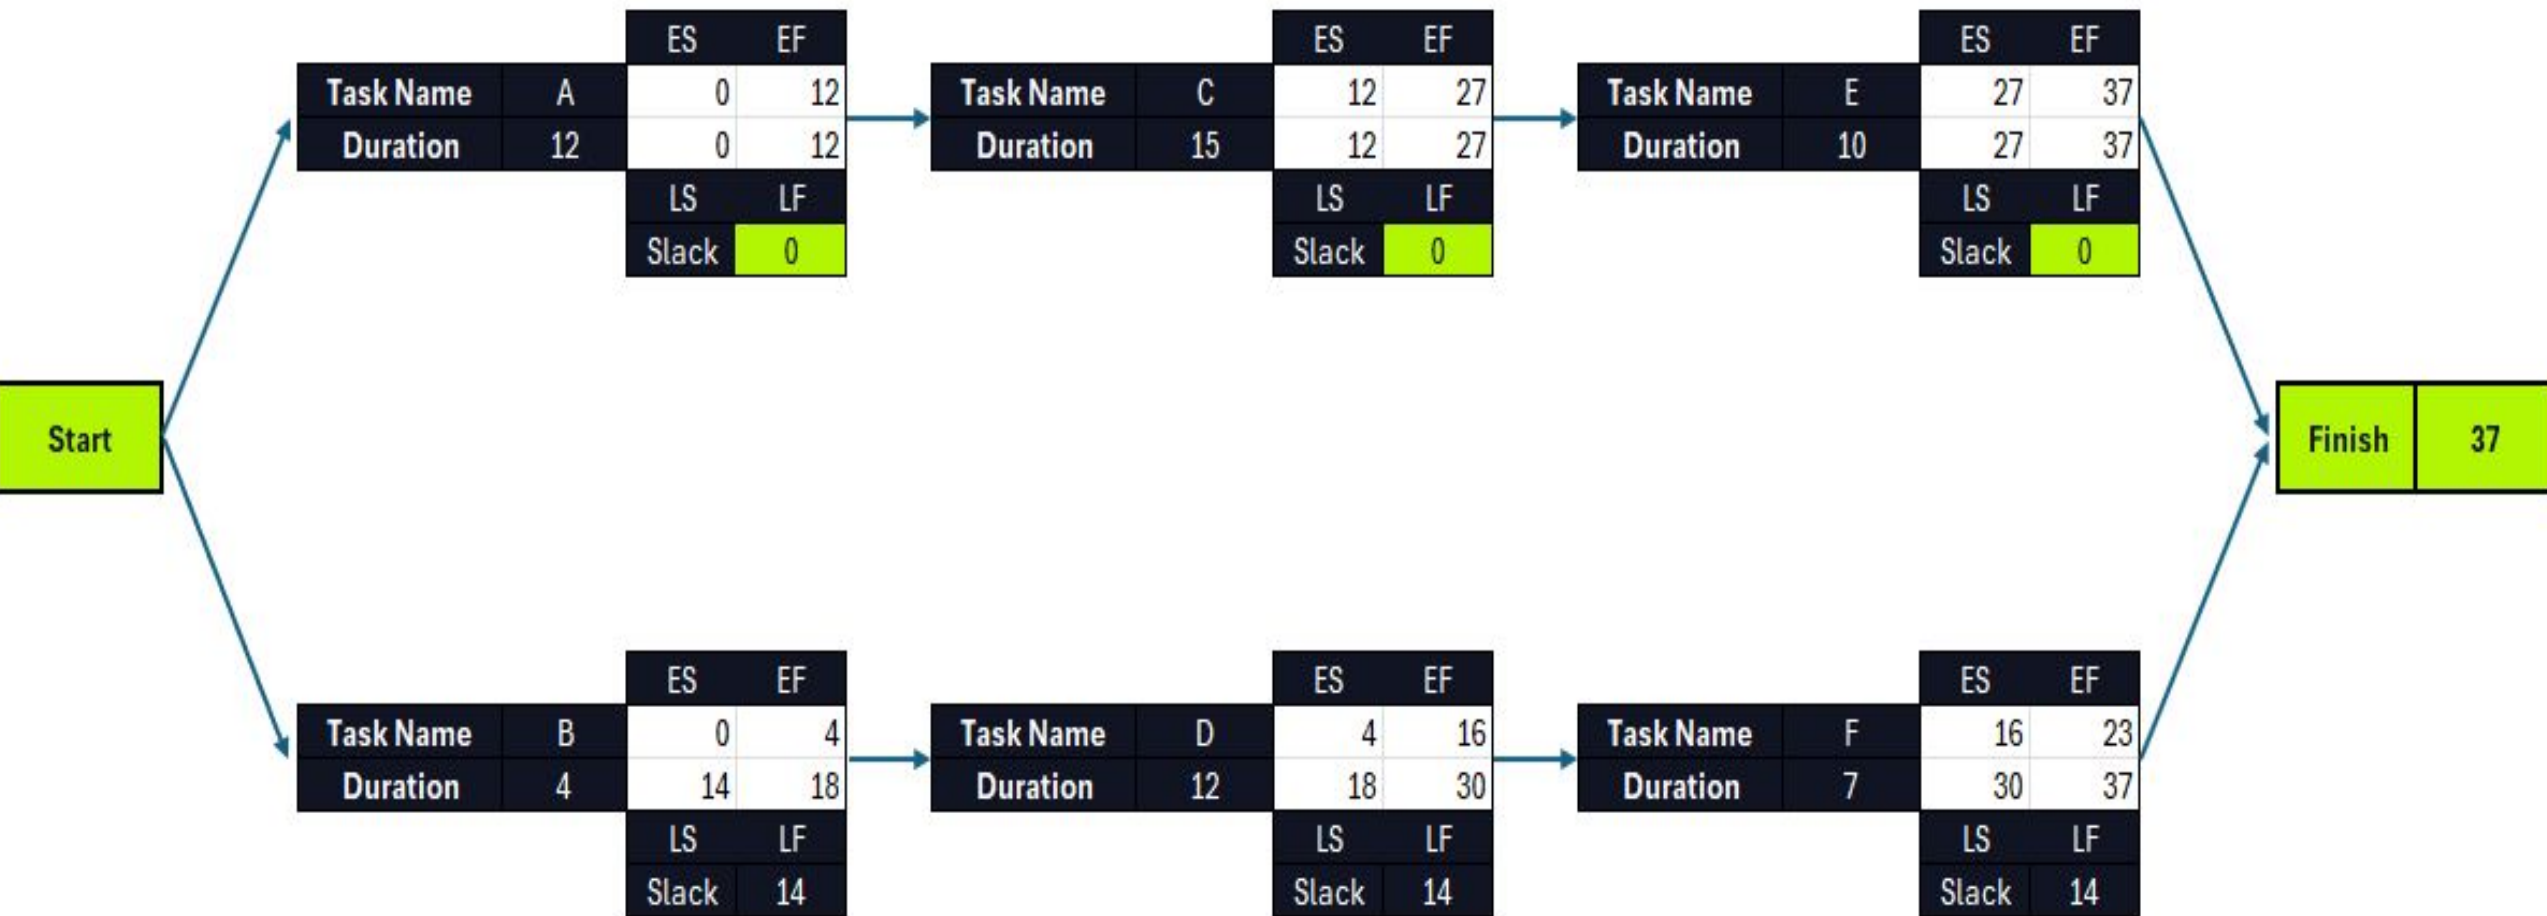

Importance of Updating Critical Path Data

- It is important to update the project schedule information to meet time goals for a project
- The critical path may change as you enter actual start and finish dates
- If you know the project completion date will slip, negotiate with the project sponsor

Critical Chain Scheduling

❑ Critical chain scheduling

- a method of scheduling that considers limited resources when creating a project schedule and includes buffers to protect the project completion date

❑ Uses the **Theory of Constraints (TOC)**

- a management philosophy developed by Eliyahu M. Goldratt and introduced in his book *The Goal*.

❑ Attempts to minimize **multitasking**

- when a resource works on more than one task at a time

Buffers and Critical Chain

- A **buffer** is additional time to complete a task
- **Murphy's Law** states that if something **can** go wrong, it will
- **Parkinson's Law** states that work expands to fill the time allowed
- In traditional estimates, people often add a buffer to each task and use it if it's needed or not
- Critical chain scheduling removes buffers from individual tasks and instead creates
 - a **project buffer** or additional time added before the project's due date
 - **feeding buffers** or additional time added before tasks on the critical path

Program Evaluation and Review Technique (PERT)

- ▣ **PERT** is a network analysis technique used to estimate project duration when there is a high degree of uncertainty about the individual activity duration estimates
- ▣ PERT uses **probabilistic time estimates**
 - duration estimates based on using optimistic, most likely, and pessimistic estimates of activity durations, or a three-point estimate

PERT Formula and Example

▶ PERT weighted average =
$$\frac{\text{optimistic time} + 4 \times \text{most likely time} + \text{pessimistic time}}{6}$$

▶ Example:
PERT weighted average =
$$\frac{8 \text{ workdays} + 4 \times 10 \text{ workdays} + 24 \text{ workdays}}{6} = \mathbf{12 \text{ days}}$$

where optimistic time = 8 days
most likely time = **10 days**, and
pessimistic time = 24 days

Therefore, you'd use **12 days** on the network diagram instead of 10 when using PERT for the above example

Agile and Time Management

- The core values of the Manifesto for Agile Software Development are
 - Customer collaboration over contract negotiation
 - Responding to change by following a plan
- The product owner defines and prioritizes the work to be done within a sprint, so collaboration and time management are designed into the process
- Teams focus on producing a useful product in a specified timeframe with strong customer input
- Don't emphasize defining all the work before scheduling it

Schedule Control Suggestions

- Perform reality checks on schedules
- Allow for contingencies
- Don't plan for everyone to work at 100% capacity all the time
- Hold progress meetings with stakeholders and be clear and honest in communicating schedule issues

Controlling the Schedule

- Goals are to know the status of the schedule, influence factors that cause schedule changes, determine that the schedule has changed, and manage changes when they occur
- Tools and techniques include
 - Progress reports
 - A schedule change control system
 - Project management software, including schedule comparison charts like the tracking Gantt chart
 - Variance analysis, such as analyzing float or slack
 - Performance management, such as earned value (chapter 7)

Reality Checks on Scheduling

- First review the draft schedule or estimated completion date in the project charter
- Prepare a more detailed schedule with the project team
- Make sure the schedule is realistic and followed
- Alert top management well in advance if there are schedule problems

Working with People Issues

- Strong leadership helps projects succeed more than good PERT charts
- Project managers should use
 - empowerment
 - incentives
 - discipline
 - negotiation

Chapter Summary

- Project time management is often cited as the main source of conflict on projects, and most IT projects exceed time estimates
- Main processes include
 - Plan schedule management
 - Define activities
 - Sequence activities
 - Estimate activity resources
 - Estimate activity durations
 - Develop schedule
 - Control schedule
